

| ID | Task Name | Duration | Start | Half 2, 2016 | | | | | | | Half 1, 2017 | | | Half 2, 2017 | | | Half 1, 2018 | | | Half 2, 2018 | | | Half 1, 2019 | | | Half 2, 2019 | | | Half | | |
|----|------------------------------------------------------------------------------------------------------|-----------------|---------------------|------------------------------------------|---|---|---|---|---|---|--------------|---|---|--------------|---|---|--------------|---|---|--------------|---|---|--------------|---|---|--------------|---|---|------|--|--|
| | | | | J | S | N | J | M | M | J | S | N | J | M | M | J | S | N | J | M | M | J | S | N | J | S | N | J | | | |
| 1 | Trauma Registry development P20 project | 490 days | Mon 24/10/16 | [Timeline bar from 24/10/16 to 27/03/17] | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 2 | Conduct baseline assessment of current data collection practices (e.g MVA, pathology, police) | 1 day? | Wed 08/03/17 | [Timeline bar on 08/03/17] | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 3 | Literature review of trauma registries and data guidelines | 20 days | Mon 24/10/16 | [Timeline bar from 24/10/16 to 13/11/16] | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 4 | regional and local trauma registries and data collection forms | 20 days | Mon 21/11/16 | [Timeline bar from 21/11/16 to 11/12/16] | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 5 | compile data variables that need to be collected (core data elements) | 20 days | Mon 19/12/16 | [Timeline bar from 19/12/16 to 08/01/17] | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 6 | Develop a research proposal and obtain for ethical approval | | | [Timeline bar from 08/01/17 to 08/06/17] | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 7 | Propose a research topic | 10 days | Mon 16/01/17 | [Timeline bar from 16/01/17 to 25/01/17] | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 8 | Literature review summary | 25 days | Mon 06/02/17 | [Timeline bar from 06/02/17 to 01/03/17] | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 9 | Proposal write up | 15 days | Mon 20/03/17 | [Timeline bar from 20/03/17 to 04/04/17] | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 10 | Team finalising and approving the proposal | 5 days | Thu 13/04/17 | [Timeline bar from 13/04/17 to 18/04/17] | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 11 | Submission of proposal for ethical approval | 35 days | Thu 20/04/17 | [Timeline bar from 20/04/17 to 20/05/17] | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 12 | Obtaining ethical approval | 1 day? | Thu 08/06/17 | [Timeline bar on 08/06/17] | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 13 | Finalize data abstraction tool | 60 days | Fri 09/06/17 | [Timeline bar from 09/06/17 to 08/08/17] | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 14 | Hold stakeholder meetings | 70 days | Mon 27/03/17 | [Timeline bar from 27/03/17 to 06/05/17] | | | | | | | | | | | | | | | | | | | | | | | | | | | |

Project: Trauma timeline
Date: Wed 08/03/17

| | | | | | |
|--------------------|--|-----------------------|--|--------------------|--|
| Task | | Inactive Summary | | External Tasks | |
| Split | | Manual Task | | External Milestone | |
| Milestone | | Duration-only | | Deadline | |
| Summary | | Manual Summary Rollup | | Progress | |
| Project Summary | | Manual Summary | | Manual Progress | |
| Inactive Task | | Start-only | | | |
| Inactive Milestone | | Finish-only | | | |

| ID | Task Name | Duration | Start | Half 2, 2016 | | | Half 1, 2017 | | | Half 2, 2017 | | | Half 1, 2018 | | | Half 2, 2018 | | | Half 1, 2019 | | | Half 2, 2019 | | | Half |
|----|-------------------------------------------------------------------------|----------|-----------------|--------------|---|---|--------------|---|---|--------------|---|---|--------------|---|---|--------------|---|---|--------------|---|---|--------------|---|---|------|
| | | | | J | S | N | J | M | M | J | S | N | J | M | M | J | S | N | J | M | M | J | S | N | J |
| 15 | Train research assistants on use of Data data abstraction tool | 40 days | Mon 03/07/17 | | | | | | | | | | | | | | | | | | | | | | |
| 16 | Trial test the data collection | 70 days | Mon 28/08/17 | | | | | | | | | | | | | | | | | | | | | | |
| 17 | Finalize the data collection protocol and begin data collection process | 140 days | Mon 04/12/17 | | | | | | | | | | | | | | | | | | | | | | |
| 18 | Analyze the Registry entries and compile quarterly reports. | 60 days | Mon 18/06/18 | | | | | | | | | | | | | | | | | | | | | | |

Kagiso Ndlovu and team ,Mpapho Joseph Motsumi,Thap

01/12

Trauma team

07/09

| | | | | | | |
|------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: Trauma timeline Date: Wed 08/03/17 | Task | | Inactive Summary | | External Tasks | |
| | Split | | Manual Task | | External Milestone | |
| | Milestone | | Duration-only | | Deadline | |
| | Summary | | Manual Summary Rollup | | Progress | |
| | Project Summary | | Manual Summary | | Manual Progress | |
| | Inactive Task | | Start-only | | | |
| | Inactive Milestone | | Finish-only | | | |

CRITICAL TASKS



- Status: Complete
- Status: On Schedule
- Status: Future Task

A task is critical if there is no room in the schedule for it to slip.

[Learn more about managing your project's critical path.](#)

| Name | Start | Finish | % Complete | Remaining Work | Resource Names |
|----------------------------------------------------------------------------|-----------------|--------------|------------|----------------|--------------------------------------------------------------------------------------------------------|
| Literature review summary | Mon 06/02/17 | Wed 29/03/17 | 50% | 200 hrs | Megan Cox,Trauma team |
| Hold stakeholder meetings | Mon 27/03/17 | Fri 30/06/17 | 0% | 560 hrs | Trauma team |
| Train research assistants on use of Data data abstraction tool | Mon 03/07/17 | Fri 25/08/17 | 0% | 1,280 hrs | Kagiso Ndlovu and team ,Mpapho Joseph Motsumi,Thapelo Richard Montshiwa ,Trauma team |
| Trial test the data collection | Mon 28/08/17 | Fri 01/12/17 | 0% | 560 hrs | Trauma team |
| Finalize the data collection protocol and begin data collection process | Mon 04/12/17 | Fri 15/06/18 | 0% | 1,120 hrs | Trauma team |
| Analyze the Registry entries and compile quarterly reports. | Mon 18/06/18 | Fri 07/09/18 | 0% | 480 hrs | Trauma team |

PROJECT OVERVIEW

MON 24/10/16 FRI 07/09/18

% COMPLETE

15%


MILESTONES DUE

Milestones that are coming soon.

| Name | Finish |
|-------------------------------------------------------------|--------------|
| Obtaining ethical approval | Thu 08/06/17 |
| Trial test the data collection | Fri 01/12/17 |
| Analyze the Registry entries and compile quarterly reports. | Fri 07/09/18 |

% COMPLETE

Status for all top-level tasks. To see the status for subtasks, click on the chart and update the outline level in the Field List.

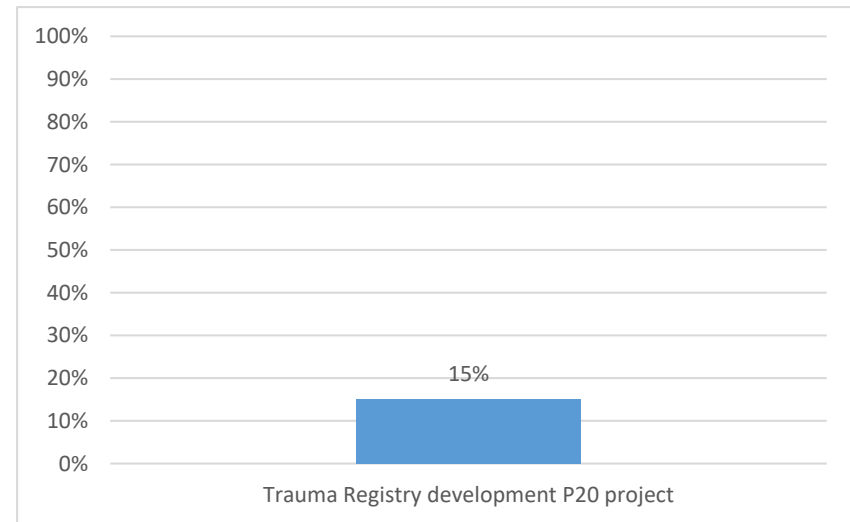

LATE TASKS

Tasks that are past due.

| Name | Start | Finish | Duration | % Complete | Resource Names |
|------|-------|--------|----------|------------|----------------|
|------|-------|--------|----------|------------|----------------|

